



कार्यालय बरेली विकास प्राधिकरण, बरेली

रामगंगा नगर आवासीय योजना सेक्टर-2, बरेली (उ०प्र०)

Website : www.bdainfo.org, email : bdbareilly@gmail.com, blyda@up.nic.in

दूरभाष : 05812301640
फैक्स : 05812301299

FORM-R

ENGINEER'S CERTIFICATE

Date : 30-06-2026

Subject:

(For The Purpose of Registration of Project and for withdrawal of Money from Designated Account)

Certificate of Percentage of Completion of Construction Work of Development works of Sector-2A Greater Bareilly. The Project [UPRERA Registration Number-UP RERAPR145066] situated on the Khasra No.2m, 9m, 10m, 11& 12, 14 to 22, 24 to 26, 74 to 76, 78, 79, 81, 82, 86 to 88, 89 Ka, 89Kha, 91, 91/208, 92 to 96, 98Ka, 98Kha, 99Ka, 99Kha, 101 to 107, 110 to 113, 115, 116, 118, 120, 124, 125, 128, 129, 130, 132 to 135, 136m, 138, 139, 141, 142, 144, 146, 147, 148, 155, 156, 157, 160, 161, 162m, 162, 439, 470, 471, 472, 474, 477 to 480 Village Ahirola And Mohanpur Urf Ramnagar Demarcated by its boundaries (latitude and longitude of the end points)

latitude 28.366548 N

latitude 28.366548 N

Longitude 79.486105 E

Longitude 79.486105 E

to the North_ to the South_ to the East_ to the West of village Ahirola and Mohanpur Urf Ramnagar, Tehsil Sadar Bareilly, Bareilly Development Authority, Bareilly, District Bareilly, PIN-243001 admeasuring 268515 sq.mts. area being developed by Bareilly Development Authority, Bareilly.

I, Sandeep Kumar, EE have undertaken assignment as Executive Engineer, certifying Percentage of Completion Work of the Plots development of the Project, situated on the Khasra No.2m, 9m, 10m, 11& 12, 14 to 22, 24 to 26, 74 to 76, 78, 79, 81, 82, 86 to 88, 89 Ka, 89Kha, 91, 91/208, 92 to 96, 98Ka, 98Kha, 99Ka, 99Kha, 101 to 107, 110 to 113, 115, 116, 118, 120, 124, 125, 128, 129, 130, 132 to 135, 136m, 138, 139, 141, 142, 144, 146, 147, 148, 155, 156, 157, 160, 161, 162m, 162, 439, 470, 471, 472, 474, 477 to 480 Village Ahirola And Mohanpur Urf Ramnagar, Tehsil Sadar, District Bareilly, PIN-243001 admeasuring 268515.00 sq.mts. area being developed by Bareilly Development Authority, Bareilly.

This is to certify that I have undertaken assignment of certifying estimated cost and expenses incurred on actual on site construction for the Real Estate Project mentioned above.

1. Following technical professionals were consulted by me for verification /for certification of the cost:

- Shri Sandeep Kumar, Executive Engineer (Incharge), Bareilly Development Authority, Bareilly.
- Shri Ajay Kumar Yadav, AE (Civil), Shri Manoj Kumar, AE (Electrical), Bareilly Development Authority
- Shri S.P. Singh, JTC (Civil), Shri Sandeep Kumar JE (Electrical) as Site Engineers to supervise the work.

14.07.2026
S.P.S.

14.07.2026
(S.S.)

The project is still ongoing. We have estimated the cost of the completion of the civil, MEP and allied works, of the Building(s) of the project. Our estimated cost calculations are based on the drawings/plans made available to us for the project under reference by the Promoter, Developer and Consultants and the Schedule of items and quantity for the entire work as calculated by Quantity Surveyor appointed by the Promoter, and the fair assumption of the cost of material, labour and other inputs made by developer, and the site inspection carried out by us.

3. We estimate the Total Cost for completion of the project under reference as Rs..17291.48 lacs (Total of S.No. 1 in Tables A and B) including cost of development of common facilities. The estimated Total Cost of project is with reference to the Civil, MEP and allied works required to be completed for obtaining occupation certificate/completion certificate for the building(s) from the concerned Competent Authority under whose jurisdiction the previously mentioned project is being implemented.

4. The estimated actual cost incurred till date 31-03-2026 is calculated at Rs...16581.38 lacs (Total of S. No. 2 in Tables A and B). The amount of Estimated Cost Incurred is calculated based on amount of Total Estimated Cost.

5. The Balance cost of Completion of the Civil, MEP and Allied works of the Building(s) of the subject project to obtain Occupation Certificate/Completion Certificate from the Competent Authority is estimated at Rs. 710.10 lacs (Total of S.No. 4 in Tables A and B).

6. I certify that the Cost of Civil, MEP and allied work for the aforesaid Project as completed on dated 13-08-2028 is as given in Tables A and B below :

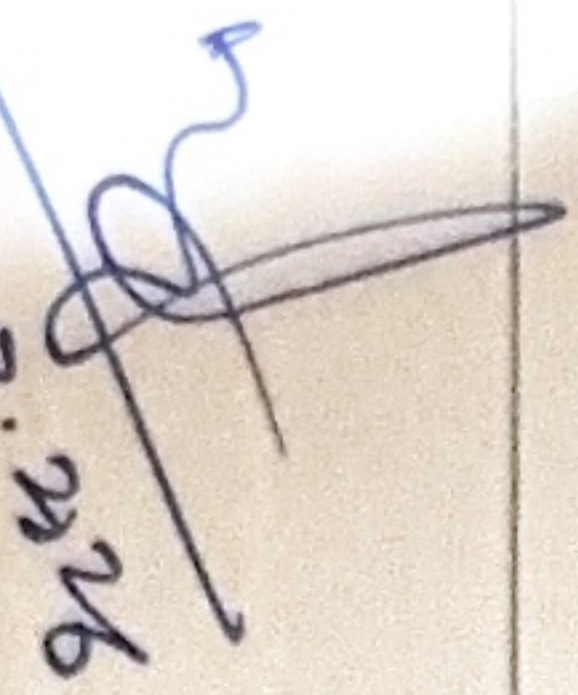
Table A

Building/Wing/Tower bearing Number **NIL** or called _____

(To be prepared separately for each Building /Wing of the Real Estate Project/Phases. In case of more than one building, label as Table-A1, A2, A3 etc.)

S.No.	Particulars	Amounts
1	Total Estimated cost of the building/wing as on date of Building Permission from Competent Authority. (based on the original Estimated cost)	NA
2	Cost incurred as on Date (Based on the actual cost incurred as per records)	NA
3	Value of Work done in Percentage (as Percentage of the estimated cost) (1*100/2)	NA
4	Balance Cost to be incurred (Based on Estimated Cost) (1-2)	NA
5	Cost incurred on Additional/ Extra items not included in the Estimated Cost (Annexure A)	NA
6	Work done in percentage (as Percentage of Estimated Cost plus additional/Extra items (1*100)/(2+5)	NA

(Enclose separate sheets for the cost calculations for each unit/building or tower)


14.07.2026
J.T.C

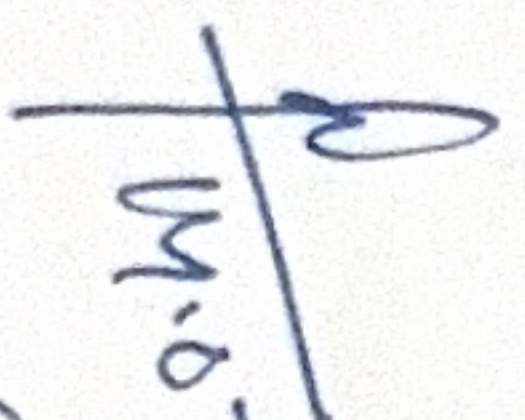

14.07.2026
(A8)

TABLE B

Internal & External Development works and common amenities
(To be prepared for the entire registered phase of the Real Estate Project)

S.No.	Particulars	Amounts (In Lacs)
1	Total Estimated cost of the Internal and External Development Works including common amenities and facilities in the layout as on date of Permission from Competent Authority (based on the original Estimated Cost).	17291.480
2	Cost incurred as on (based on the actual cost incurred as per records)	16581.380
3	Work done in Percentage (as Percentage of the estimated cost) (1*100/2)	95.89%
4	Balance Cost to be Incurred (Based on Estimated Cost) (1-2)	710.10
5	Cost incurred on Additional/ Extra Items not included in the Estimated Cost (Annexure A)	NIL
6	Work done in percentage (as Percentage of Estimated Cost plus additional/Extra items (1*100)/(2+5)	95.89%
(Enclose separate sheet for the cost calculations)		

Signature of Engineer-

Name

Sandeep Kumar

Address

Executive Engineer, Bareilly Development Authority, Bareilly.

Aadhar No.

NA

PAN No.

AAALB0169K

(License No.NA..... Of AuthorityNA.....)

Annexure A - NA

List of Extra / Additional Items executed with Cost
(which were not part of the original Estimate of Total Cost)
